Schedule B -- Accelerated Schedule for the Planning, Design and Construction of the Chino Creek Well Field

ID	Task Name	Start	Finish
1			
2	**Prepare Project Description**	**Mon 4/2/07**	**Fri 8/31/07**
3	Prepare Draft Project Description	Mon 4/2/07	Fri 4/27/07
4	Circulate and Revise Draft Project Description	Mon 4/30/07	Fri 5/25/07
5	Finalize Draft Project Description	Mon 5/28/07	Fri 6/8/07
6	Prepare Screening-Level Initial Study	Mon 6/11/07	Fri 8/31/07
7			
8	**Select Consultants**	**Mon 4/30/07**	**Fri 7/20/07**
9	Select CEQA Consultant	Mon 4/30/07	Fri 7/20/07
10	Select Well Design Consultant	Mon 4/30/07	Fri 7/20/07
11	Select Facilities Design Consultant	Mon 4/30/07	Fri 7/20/07
12	Select Program Manager	Mon 4/30/07	Fri 7/20/07
13			
14	**Select Well Sites**	**Mon 9/3/07**	**Fri 8/15/08**
15	Develop Three Well Field Alternatives	Mon 9/3/07	Fri 9/28/07
16	Determine Property Ownership in Each Well Field Alternative	Mon 10/1/07	Fri 10/26/07
17	Select Alternative Well Sites	Mon 10/29/07	Fri 11/23/07
18	**Implement Well Site Investigation Program**	**Mon 9/3/07**	**Fri 5/23/08**
19	Develop Investigation Plan	Mon 9/3/07	Fri 9/28/07
20	Negotiate Access to Test Sites	Mon 11/26/07	Fri 1/18/08
21	Obtain Permits	Mon 1/21/08	Fri 1/25/08
22	Prepare Bid Package	Mon 10/1/07	Fri 11/9/07
23	Advertise	Mon 11/12/07	Fri 12/14/07
24	Select Contractor	Fri 12/14/07	Fri 12/14/07
25	Negotiate Contract	Mon 12/17/07	Fri 1/11/08
26	Construct Test Wells, Run Stress Test and WQ Tests	Mon 1/21/08	Fri 5/9/08
27	Characterize Production Requirements and Water Quality	Fri 5/9/08	Fri 5/9/08
28	Revise Well Field Design	Mon 5/12/08	Fri 5/23/08
29	**Prepare Well Field Predesign Report**	**Mon 5/26/08**	**Fri 8/15/08**
30	Prepare Draft Report	Mon 5/26/08	Fri 6/20/08
31	Circulate and Revise Predesign Report	Mon 6/23/08	Fri 7/18/08
32	Finalize Predesign Report	Mon 7/21/08	Fri 8/15/08
33			
34	**CEQA Process for Chino Creek Well Field**	**Mon 6/23/08**	**Fri 12/5/08**
35	**Prepare Final Project Description**	**Mon 6/23/08**	**Fri 8/8/08**
36	Prepare Final Project Description	Mon 6/23/08	Fri 6/27/08
37	Circulate and Revise Final Project Description	Mon 6/30/08	Fri 7/25/08
38	Finalize Project Description	Mon 7/28/08	Fri 8/8/08
39	Prepare Initial Study	Mon 8/18/08	Fri 9/26/08
40	Prepare Mitigated Negative Declaration	Mon 9/29/08	Fri 10/10/08
41	Circulate Mitigated Negative Declaration	Mon 10/13/08	Fri 11/7/08
42	Conduct Public Meeting Regarding Mitigated Negative Declaration	Fri 11/7/08	Fri 11/7/08
43	Prepare Response to Comments	Mon 11/10/08	Fri 11/28/08
44	Prepare Final Mitigated Negative Declaration	Mon 12/1/08	Fri 12/5/08
45	IEUA Adopts Mitigated Negative Declaration	Fri 12/5/08	Fri 12/5/08
46			
47	**Select Well Field Alternative**	**Wed 4/18/07**	**Fri 12/5/08**
48	Negotiate Chino Airport/County Contribution	Wed 4/18/07	Tue 10/16/07
49	Select Well Field	Fri 12/5/08	Fri 12/5/08
50			
51	**Final Design of Well Field**	**Mon 12/8/08**	**Fri 1/8/10**
52	**Obtain Wells Sites**	**Mon 12/8/08**	**Fri 6/19/09**
53	Prepare Legal Descriptions	Mon 12/8/08	Fri 1/2/09
54	Establish Value	Mon 12/8/08	Fri 1/2/09

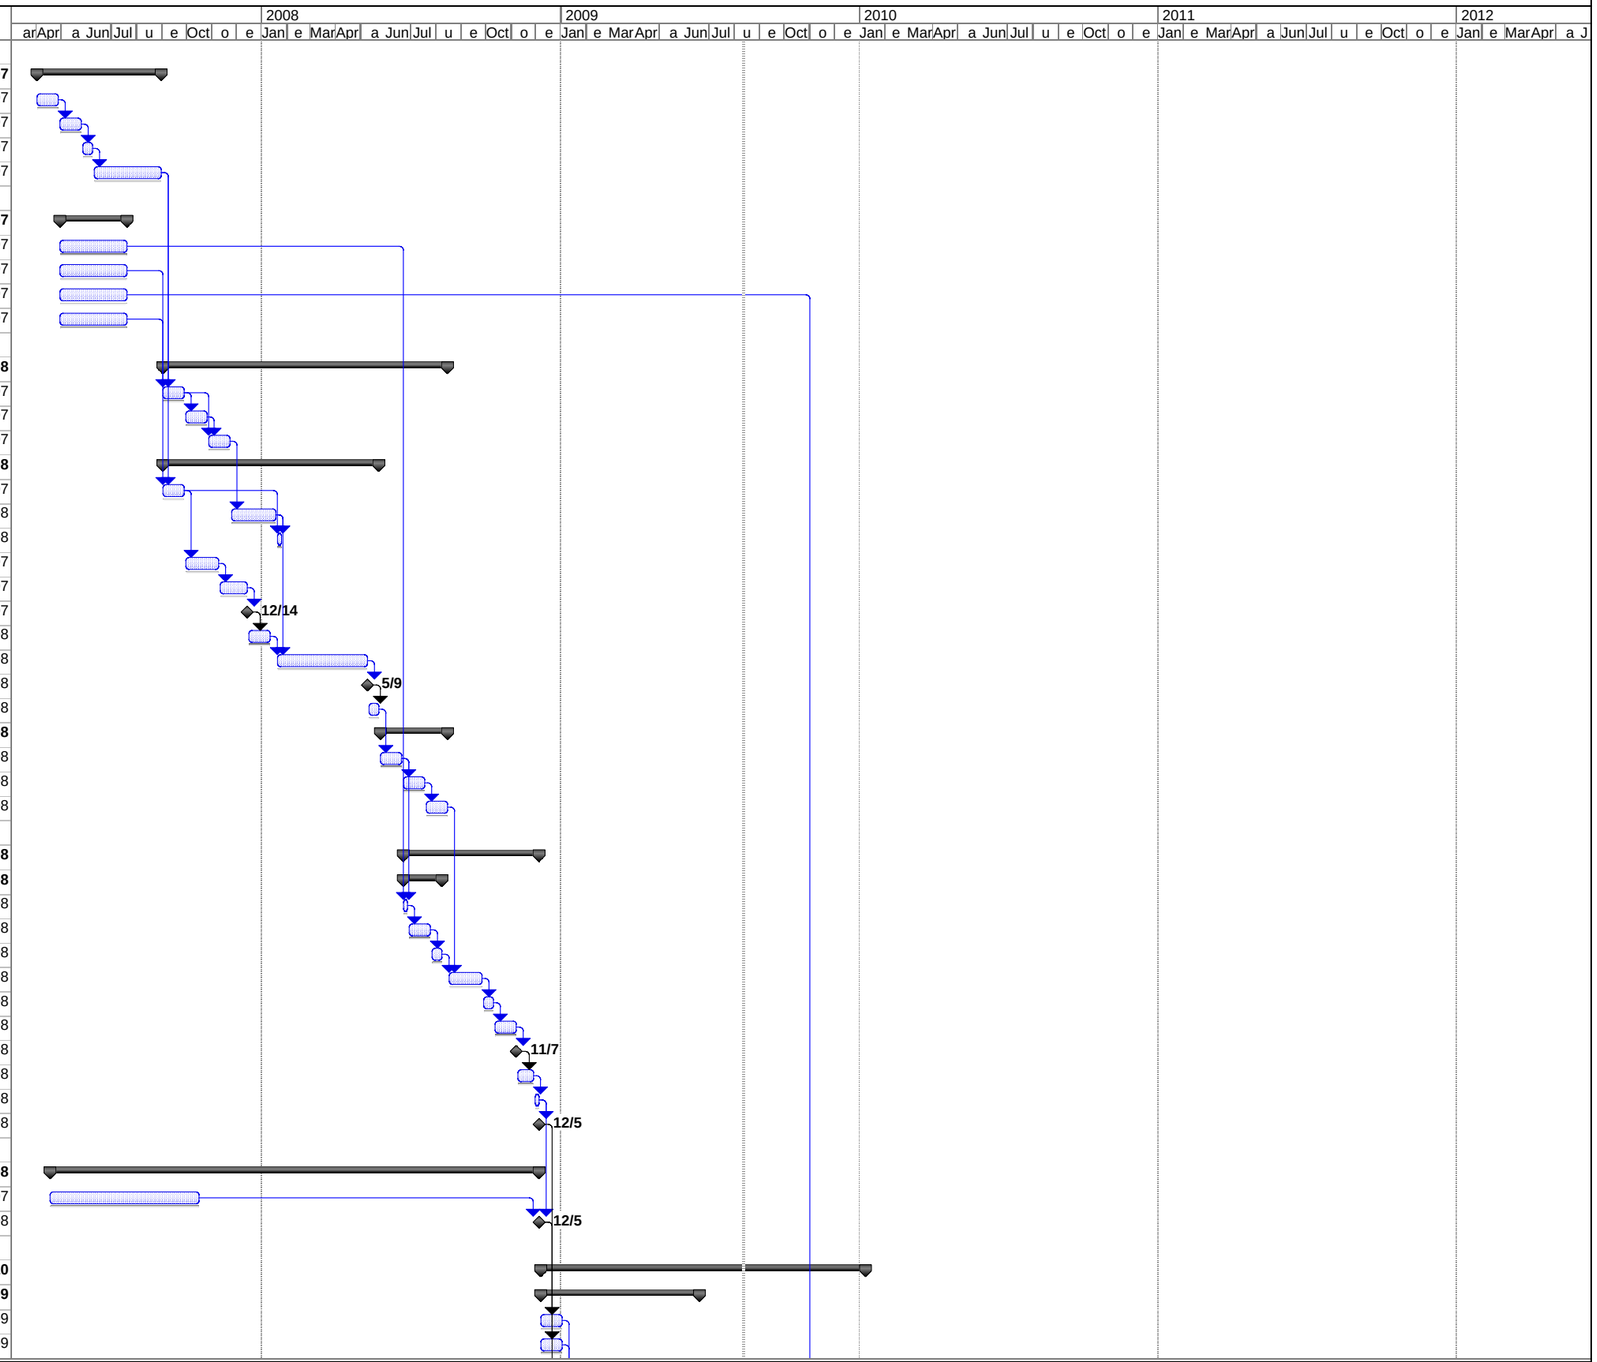

Project: 20070329 Schedule B Chino C
Date: Wed 9/12/07

Task | Progress | Summary | External Tasks | Split
Split | Milestone | Project Summary | External MileTask

Schedule B -- Accelerated Schedule for the Planning, Design and Construction of the Chino Creek Well Field

ID	Task Name	Start	Finish
55	Negotiate Site Acquisition	Mon 1/5/09	Fri 3/27/09
56	**Obtain Raw Water Pipeline Easements**	**Mon 3/30/09**	**Fri 6/19/09**
57	Prepare Legal Description	Mon 3/30/09	Fri 4/24/09
58	Negotiate Easements	Mon 4/27/09	Fri 6/19/09
59	**Prepare Final Well Field Design**	**Mon 12/8/08**	**Fri 1/8/10**
60	Prepare Plans and Specifications for Wells	Mon 12/8/08	Fri 1/30/09
61	Prepare Bid Package	Mon 2/2/09	Fri 2/27/09
62	Advertise	Mon 3/2/09	Fri 4/3/09
63	Select Contractor	Fri 4/3/09	Fri 4/3/09
64	Negotiate Contract	Mon 4/6/09	Fri 5/1/09
65	Construct Six New Wells	Mon 5/4/09	Fri 10/30/09
66	Finalize Well Production and WQ Characteristics	Fri 10/30/09	Fri 10/30/09
67	**Prepare Well Construction Report**	**Mon 11/2/09**	**Fri 1/8/10**
68	Prepare Draft Well Construction Report	Mon 11/2/09	Fri 11/27/09
69	Circulate and Review Draft	Mon 11/30/09	Fri 12/18/09
70	Finalize Well Construction Report	Mon 12/21/09	Fri 1/8/10
71			
72	**Design and Construct Pipeline, Wellhead, and Treatment Plant Improvemer**	**Mon 11/2/09**	**Fri 4/6/12**
73	Prepare 30 Percent Design Report	Mon 11/2/09	Fri 12/25/09
74	Prepare 50 Percent Design Report	Mon 12/28/09	Fri 1/29/10
75	Prepare 70 Percent Design Report	Mon 2/1/10	Fri 3/5/10
76	Prepare Final Design Report	Mon 3/8/10	Fri 4/16/10
77	Prepare Plans and Specifications	Mon 4/19/10	Fri 7/9/10
78	Prepare Bid Package	Mon 7/12/10	Fri 8/6/10
79	Advertise	Mon 8/9/10	Fri 9/10/10
80	Select Contractor	Fri 9/10/10	Fri 9/10/10
81	Negotiate Contracts	Mon 9/13/10	Fri 11/5/10
82	Construct Raw Water Pipeline	Mon 11/8/10	Fri 11/18/11
83	Construct Wellhead Improvements	Mon 11/8/10	Fri 11/18/11
84	Construct Desalter I Improvements	Mon 11/8/10	Fri 11/18/11
85	Construction Complete	Fri 11/18/11	Fri 11/18/11
86	**Prepare Construction Report**	**Mon 11/21/11**	**Fri 4/6/12**
87	Prepare Draft Construction Report	Mon 11/21/11	Fri 1/13/12
88	Circulate and Review Draft	Mon 1/16/12	Fri 3/9/12
89	Finalize Construction Report	Mon 3/12/12	Fri 4/6/12
90			
91	Start Up Testing of Improvements	Mon 11/21/11	Fri 2/10/12
92	Start of Regular Operations	Fri 2/10/12	Fri 2/10/12

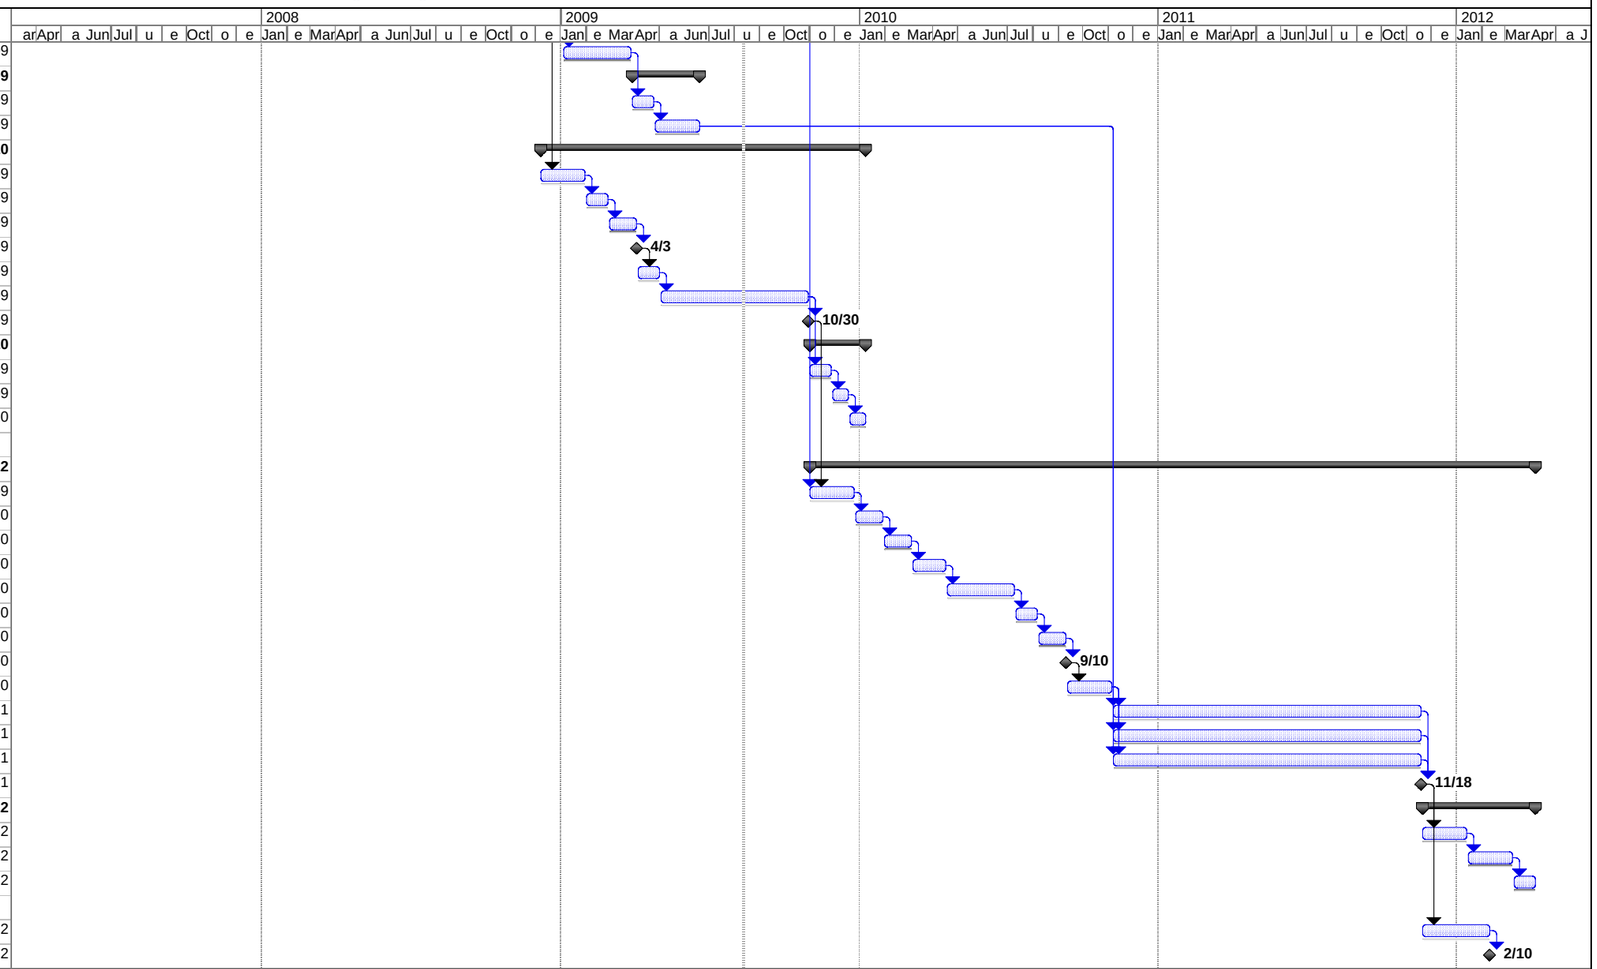

Project: 20070329 Schedule B Chino C
Date: Wed 9/12/07

Task | Progress | Summary | External Tasks | Split
Split | Milestone | Project Summary | External MileTask
